
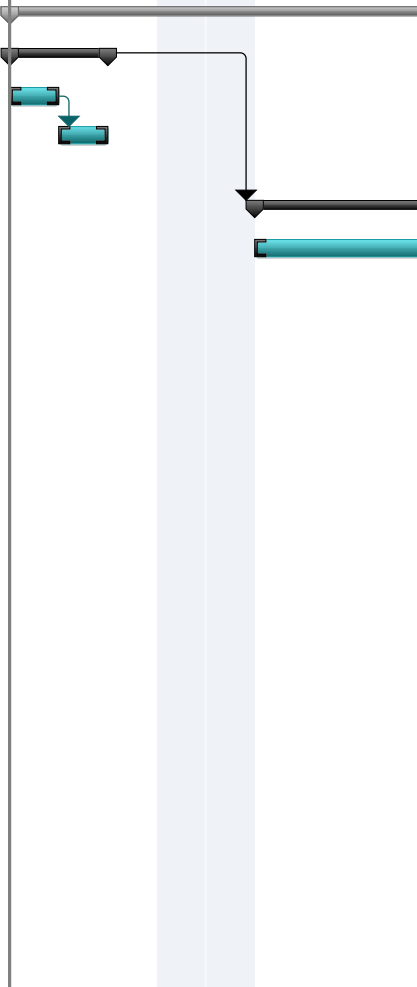


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12					Mar 4, '12					
								M	T	W	T	F	S	S	M	T	W	
0			EDR Website Redesign	138 days	Wed 2/29/12	Thu 9/13/12												
1			1 INITIATION	2 days	Wed 2/29/12	Thu 3/1/12												
2			1.1 Identify Stakeholders.	1 day	Wed 2/29/12	Wed 2/29/12												
3			1.2 Identify Human Resources.	1 day	Thu 3/1/12	Thu 3/1/12	2											
4			2 PLANNING	135 days	Mon 3/5/12	Thu 9/13/12	1											
5			2.1 Identify Stakeholder Requirements for Social Media Campaign.	17 days	Mon 3/5/12	Tue 3/27/12												
6			2.2 Identify stakeholder requirements for web-host service provider.	32 days	Wed 3/28/12	Fri 5/11/12	5											
7			2.3 Identify Stakeholder Requirements for phase 1 website redesign.	2 days	Mon 5/14/12	Tue 5/15/12	6											
8			2.4 Identify web-host service provider candidates.	42 days	Wed 5/16/12	Mon 7/16/12	7											
9			2.5 Identify web-host service provider services, costs, and constraints.	42 days	Tue 7/17/12	Thu 9/13/12	8											
10			3 EXECUTION	118 days	Tue 3/27/12	Wed 9/12/12	4											
11			3.1 Identify appropriate social media.	23 days	Tue 3/27/12	Fri 4/27/12												

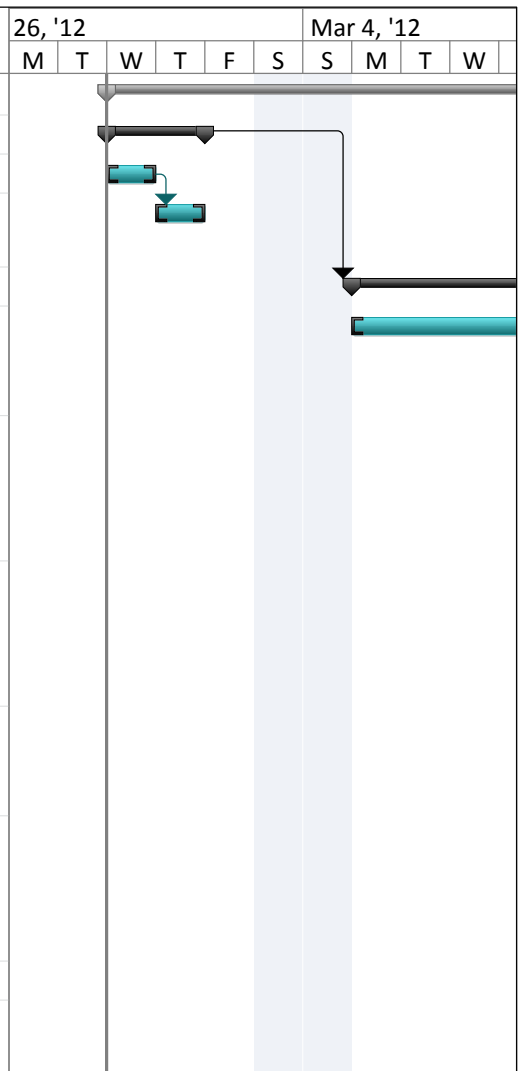

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12							Mar 4, '12			
								M	T	W	T	F	S	S	M	T	W	
12			3.2 Set up accounts for selected social media.	23 days	Mon 4/30/12	Wed 5/30/12	11											
13			3.3 Activate social media accounts.	0 days	Fri 6/1/12	Fri 6/1/12	12											
14			3.4 Create webpages specified in stakeholder requirements.	34 days	Fri 6/1/12	Thu 7/19/12	13											
15			3.5 Update vendor-hosted webpage as specified in stakeholder requirements.	34 days	Fri 7/20/12	Thu 9/6/12	14											
16			3.6 Compare services and costs of candidate web-host service providers.	4 days	Fri 9/7/12	Wed 9/12/12	15											
17			4 MONITORING & COLLABORATING	24 days	Fri 4/27/12	Wed 5/30/12	10											
18			4.1 Manage accounts through daily posts and tweets.	6 days	Fri 4/27/12	Fri 5/4/12												
19			4.2 Follow relevant posts and tweets made by others.	6 days	Mon 5/7/12	Mon 5/14/12	18											

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12						Mar 4, '12			
								M	T	W	T	F	S	S	M	T	W
20			4.3 Check the five new webpages and one vendor-hosted webpage against stakeholder requirements.	1 day	Tue 5/15/12	Tue 5/15/12	19										
21			4.4 Repair any defects.	1 day	Wed 5/16/12	Wed 5/16/12	20										
22			4.5 Publish website under privacy settings.	1 day	Thu 5/17/12	Thu 5/17/12	21										
23			4.6 Confirm that the website renders correctly in all major browsers and in smart-phone mobile device screens.	1 day	Fri 5/18/12	Fri 5/18/12	22										
24			4.7 Confirm that all links and interactive widgets work.	1 day	Mon 5/21/12	Mon 5/21/12	23										
25			4.8 Repair any rendering issues and any non-working links and widgets.	1 day	Tue 5/22/12	Tue 5/22/12	24										
26			4.9 Conduct user accepantce testing with stakeholders.	1 day	Wed 5/23/12	Wed 5/23/12	25										

Project: EDR Website Redesign Date: Sun 4/22/12		Task		External Milestone		Manual Summary Rollup	
		Split		Inactive Task		Manual Summary	
		Milestone		Inactive Milestone		Start-only	
		Summary		Inactive Summary		Finish-only	
		Project Summary		Manual Task		Deadline	
		External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12						Mar 4, '12			
								M	T	W	T	F	S	S	M	T	W
27			4.10 Confirm that the website and social media campaign meet stakeholder requirements.	1 day	Thu 5/24/12	Thu 5/24/12	26										
28			4.11 Publish website for public view.	1 day	Fri 5/25/12	Fri 5/25/12	27										
29			4.12 Confirm that website is published.	1 day	Mon 5/28/12	Mon 5/28/12	28										
30			4.13 Remove old website from public view.	1 day	Tue 5/29/12	Tue 5/29/12	29										
31			4.14 Present web-host service provider findings to stakeholders.	1 day	Wed 5/30/12	Wed 5/30/12	30										
32			5 CLOSING	3 days	Fri 5/11/12	Tue 5/15/12	17										
33			5.1 Confirm with stakeholders that phase 1 is complete.	1 day	Fri 5/11/12	Fri 5/11/12											
34			5.2 Turn over to stakeholders responsibility for maintenance of phase 1 website.	1 day	Mon 5/14/12	Mon 5/14/12	33										
35			5.3 Select web-host service provider for phase	1 day	Tue 5/15/12	Tue 5/15/12	34										
36			6 INITIATION - PHASE 2	5 days	Mon 5/14/12	Fri 5/18/12	32										

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12							Mar 4, '12			
								M	T	W	T	F	S	S	M	T	W	
37			6.1 Identify appropriate qualitative research techniques to gather user requirements.	5 days	Mon 5/14/12	Fri 5/18/12												
38			7 PLANNING	8 days	Mon 5/21/12	Wed 5/30/12	36											
39			7.1 Gather and prioritize user requirements.	5 days	Mon 5/21/12	Fri 5/25/12												
40			7.2 Confirm with stakeholders the user requirements to include in the phase 2 redesign.	3 days	Mon 5/28/12	Wed 5/30/12	39											
41			8 EXECUTION	7 days	Mon 6/4/12	Tue 6/12/12	38											
42			8.1 Update the five phase 1 webpages to include user requirements.	5 days	Mon 6/4/12	Fri 6/8/12												
43			8.2 Update vendor-hosted webpage to include user requirements.	2 days	Mon 6/11/12	Tue 6/12/12	42											
44			9 MONITORING & COLLABORATING	11 days	Wed 6/13/12	Wed 6/27/12	41											
45			9.1 Check the five updated webpages and one vendor-hosted webpage against stakeholder requirements.	1 day	Wed 6/13/12	Wed 6/13/12												

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12						Mar 4, '12			
								M	T	W	T	F	S	S	M	T	W
46			9.2 Repair any defects.	2 days	Thu 6/14/12	Fri 6/15/12	45										
47			9.3 Publish the website under privacy setting. Use a new web host if applicable.	1 day	Mon 6/18/12	Mon 6/18/12	46										
48			9.4 Confirm that the website renders correctly in all major browsers and in smart-phone mobile device screens.	1 day	Tue 6/19/12	Tue 6/19/12	47										
49			9.5 Confirm that all links and interactive widgets work.	1 day	Wed 6/20/12	Wed 6/20/12	48										
50			9.6 Repair any rendering issues and any non-working links and widgets.	1 day	Thu 6/21/12	Thu 6/21/12	49										
51			9.7 Conduct user accepantce testing with stakeholders.	1 day	Fri 6/22/12	Fri 6/22/12	50										
52			9.8 Confirm that the website meets phase 2 requirements.	1 day	Mon 6/25/12	Mon 6/25/12	51										
53			9.9 Publish the website for public view.	1 day	Tue 6/26/12	Tue 6/26/12	52										

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	26, '12						Mar 4, '12			
								M	T	W	T	F	S	S	M	T	W
54			9.10 Confirm that the website is published.	1 day	Wed 6/27/12	Wed 6/27/12	53										
55			10 CLOSING	1 day	Wed 6/20/12	Wed 6/20/12	44										
56			10.1 Confirm with stakeholders that phase 2 is complete.	1 day	Wed 6/20/12	Wed 6/20/12											

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

			Mar 11, '12							Mar 18, '12							Mar 25, '12							Apr 1, '12							Apr 8, '12							Apr
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

--

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

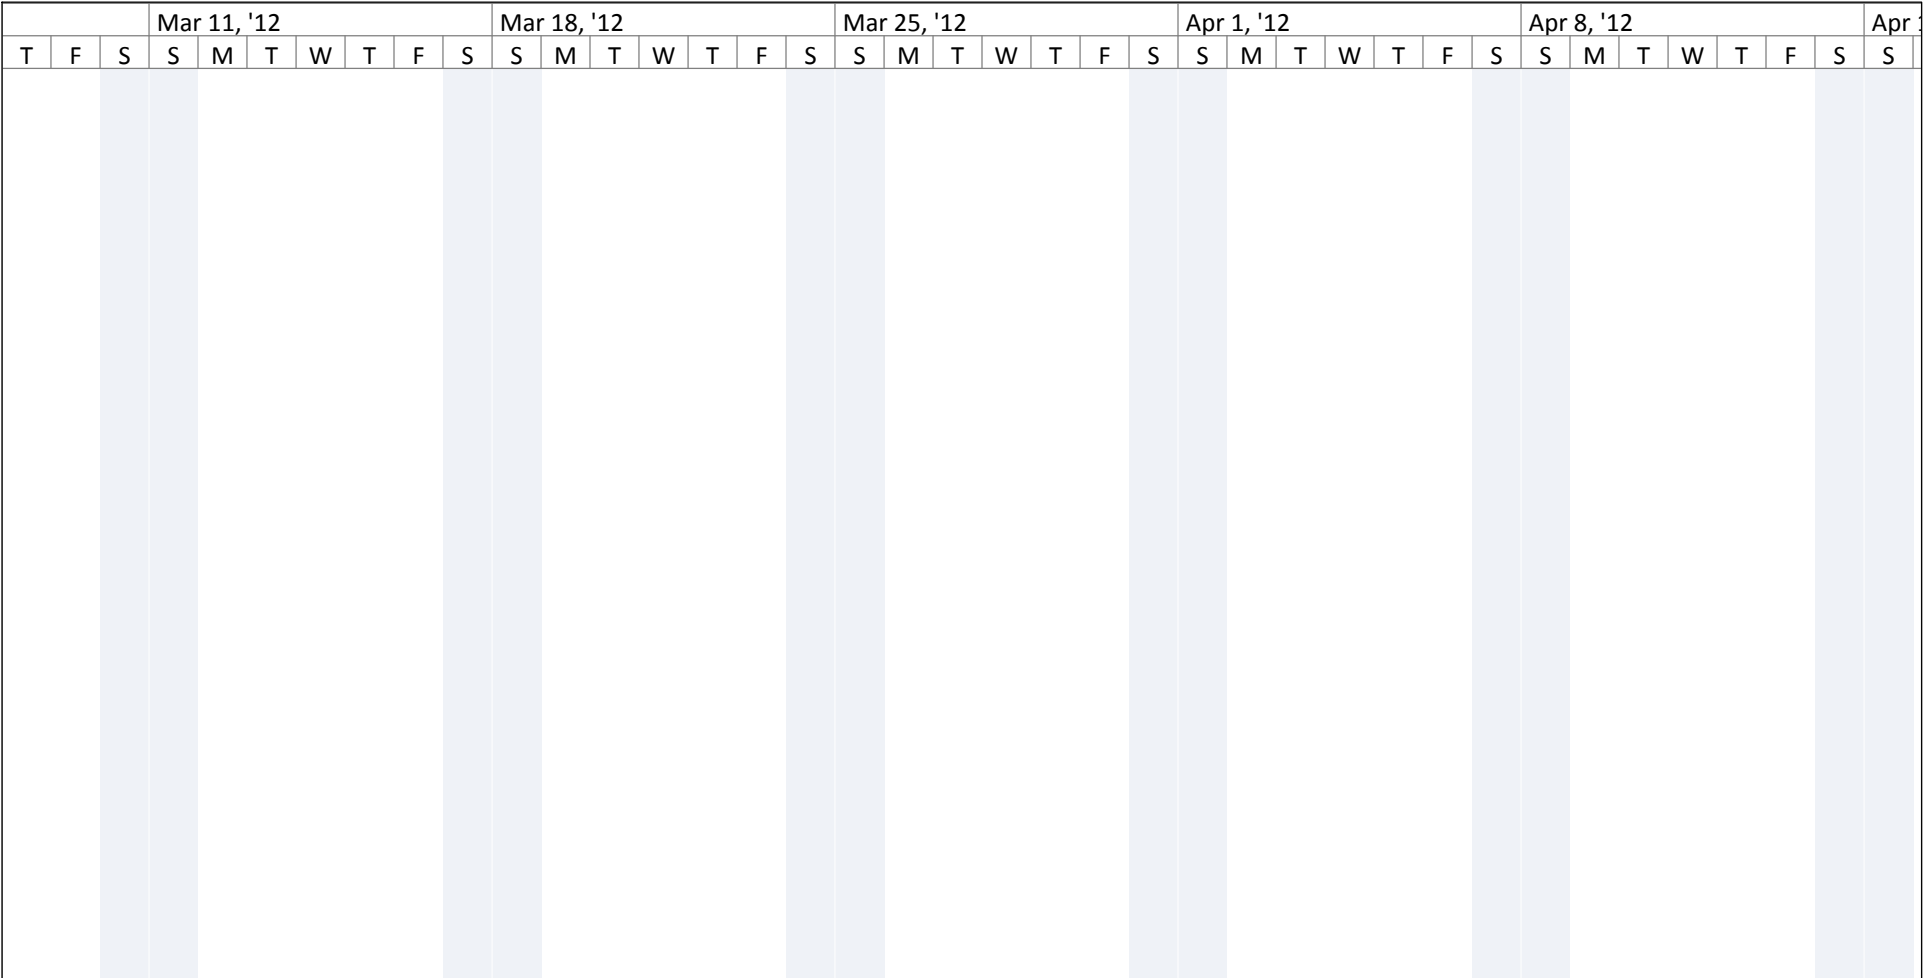

Project: EDR Website Redesign
Date: Sun 4/22/12

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

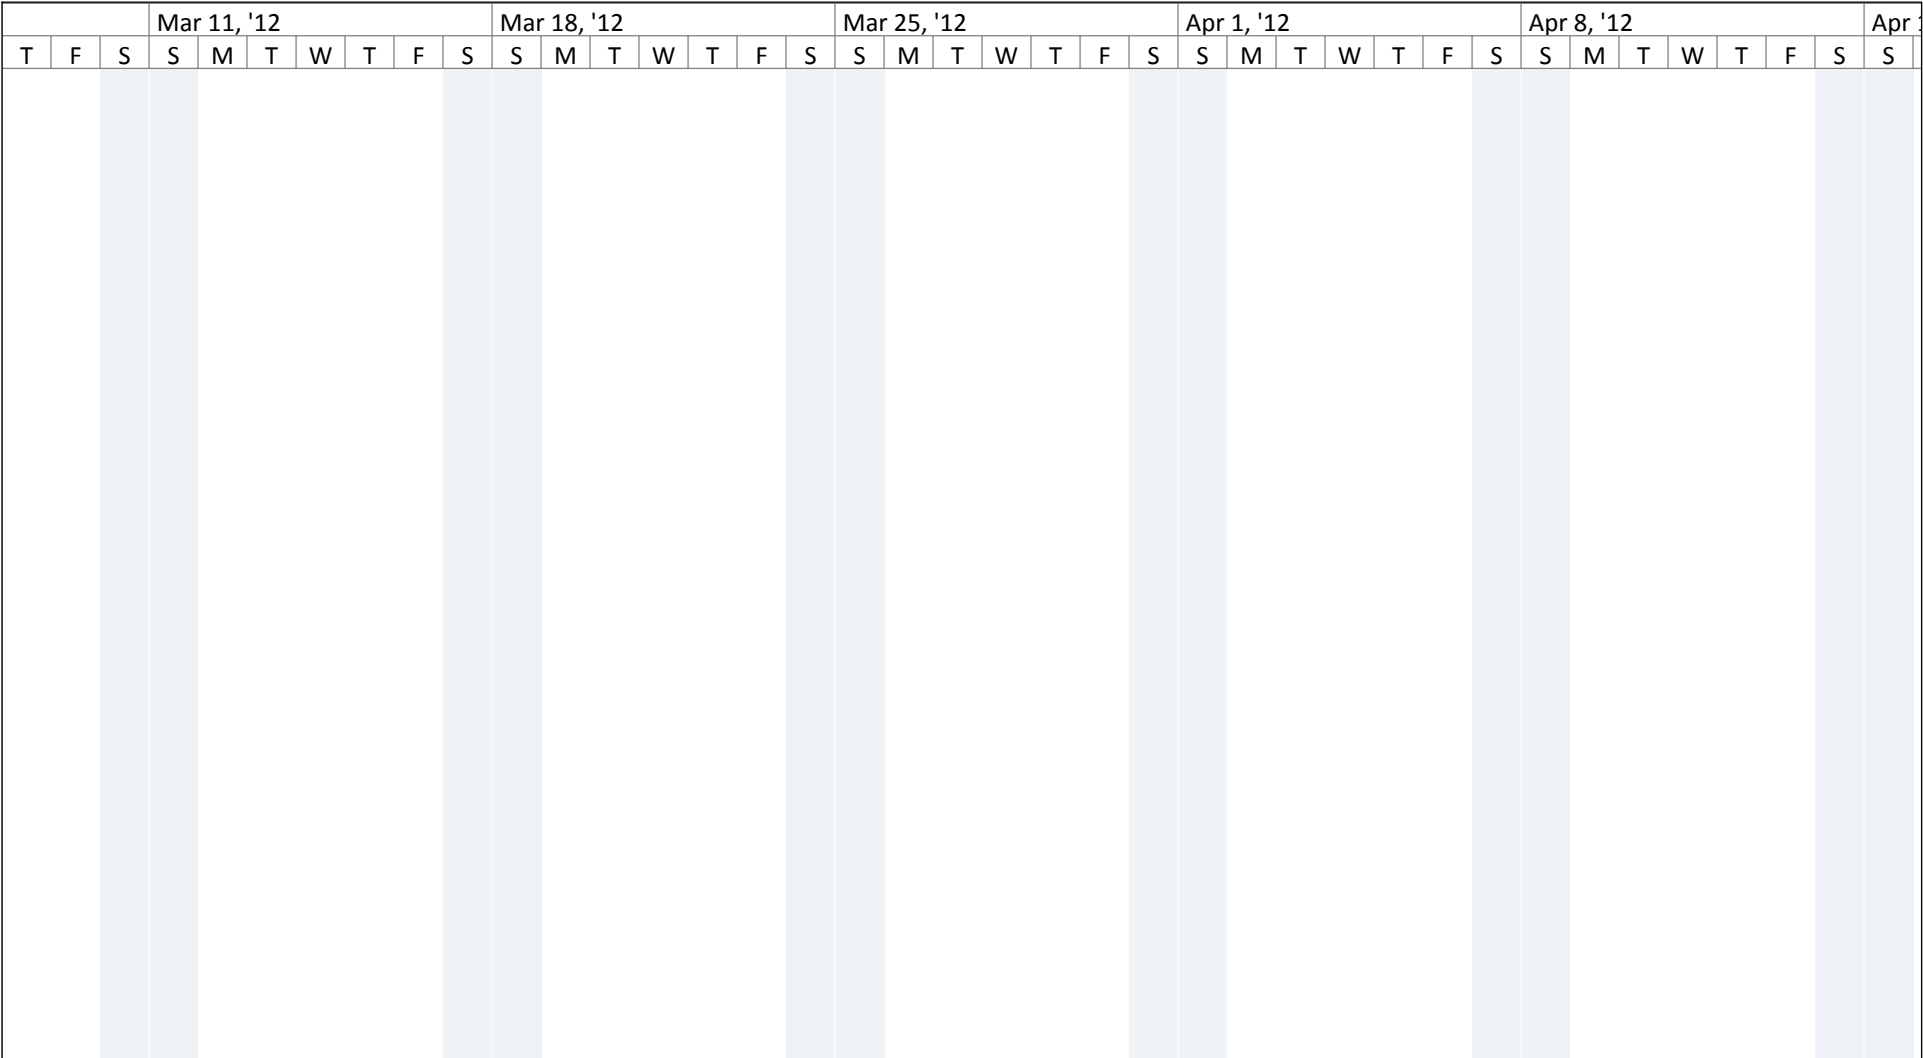

Project: EDR Website Redesign
Date: Sun 4/22/12

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

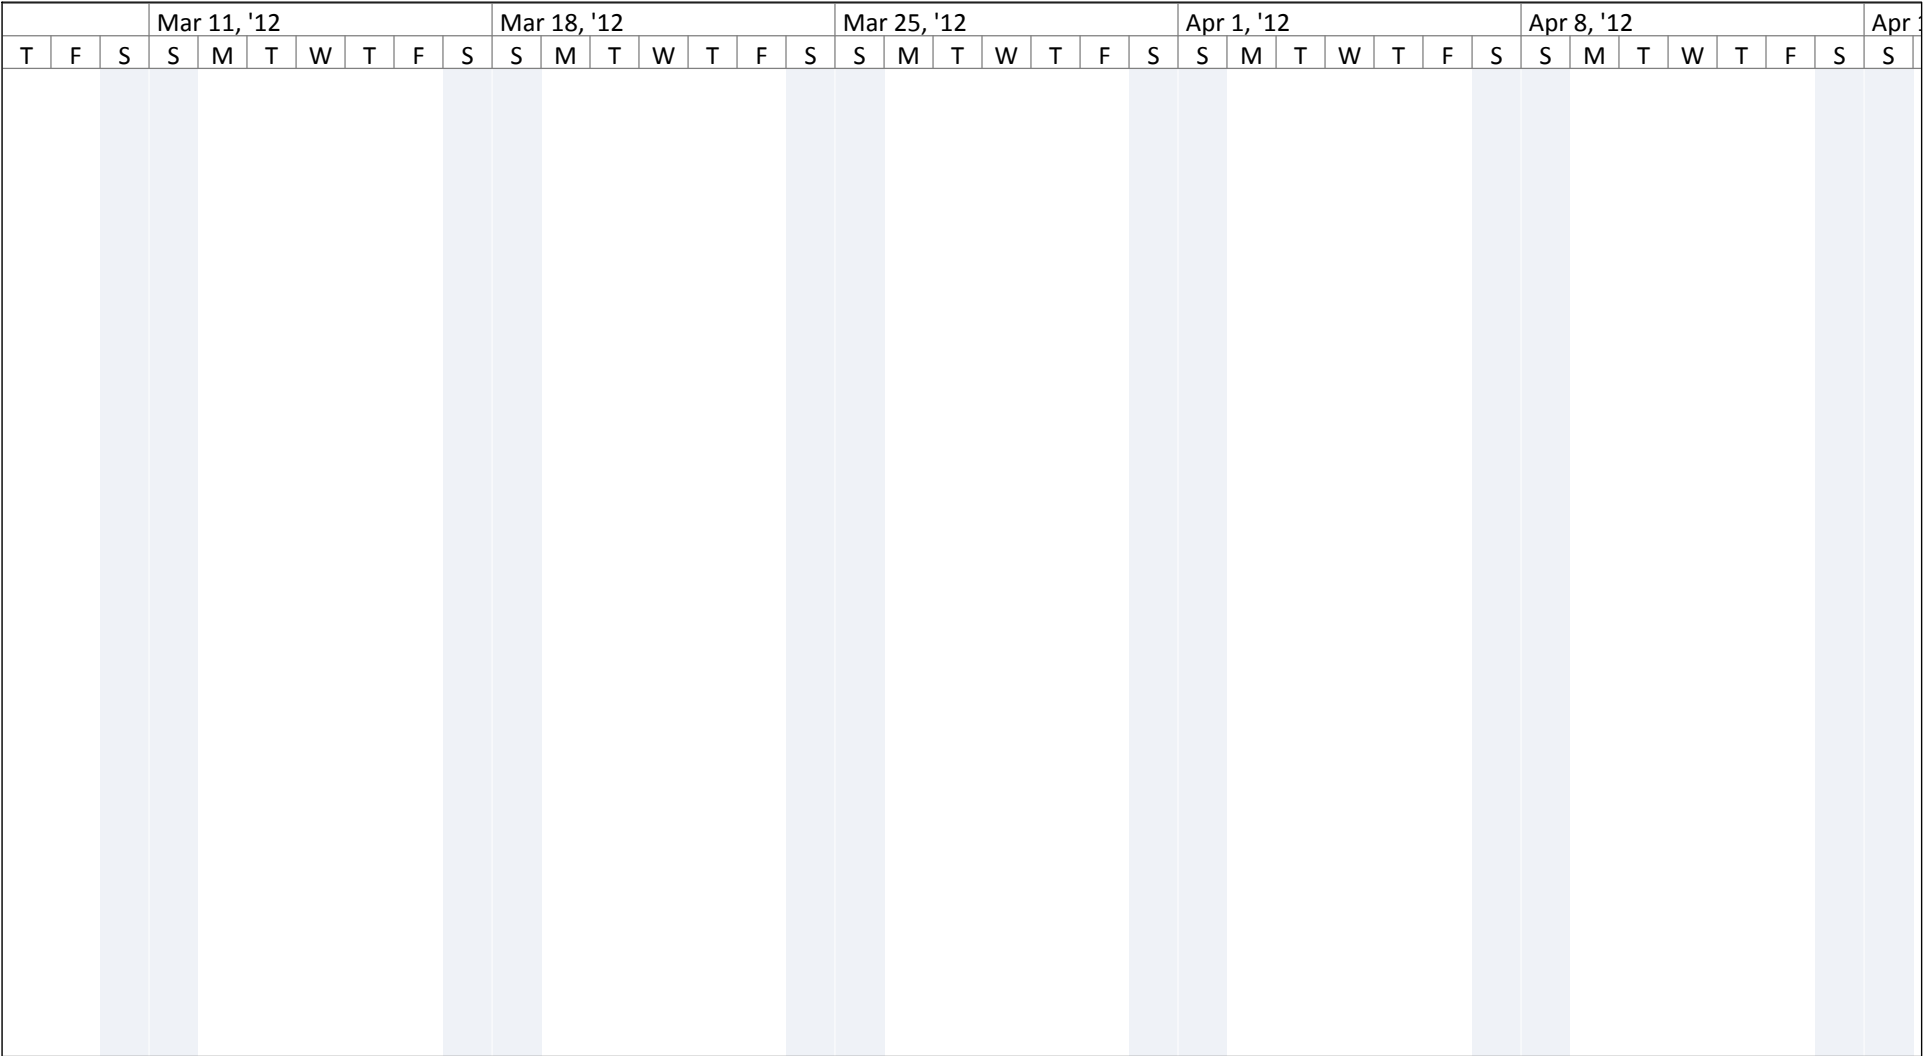

Project: EDR Website Redesign
Date: Sun 4/22/12

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

			Mar 11, '12							Mar 18, '12							Mar 25, '12							Apr 1, '12							Apr 8, '12							Apr
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Project: EDR Website Redesign

Date: Sun 4/22/12

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary


Start-only

Finish-only


Deadline

Progress


Page 13

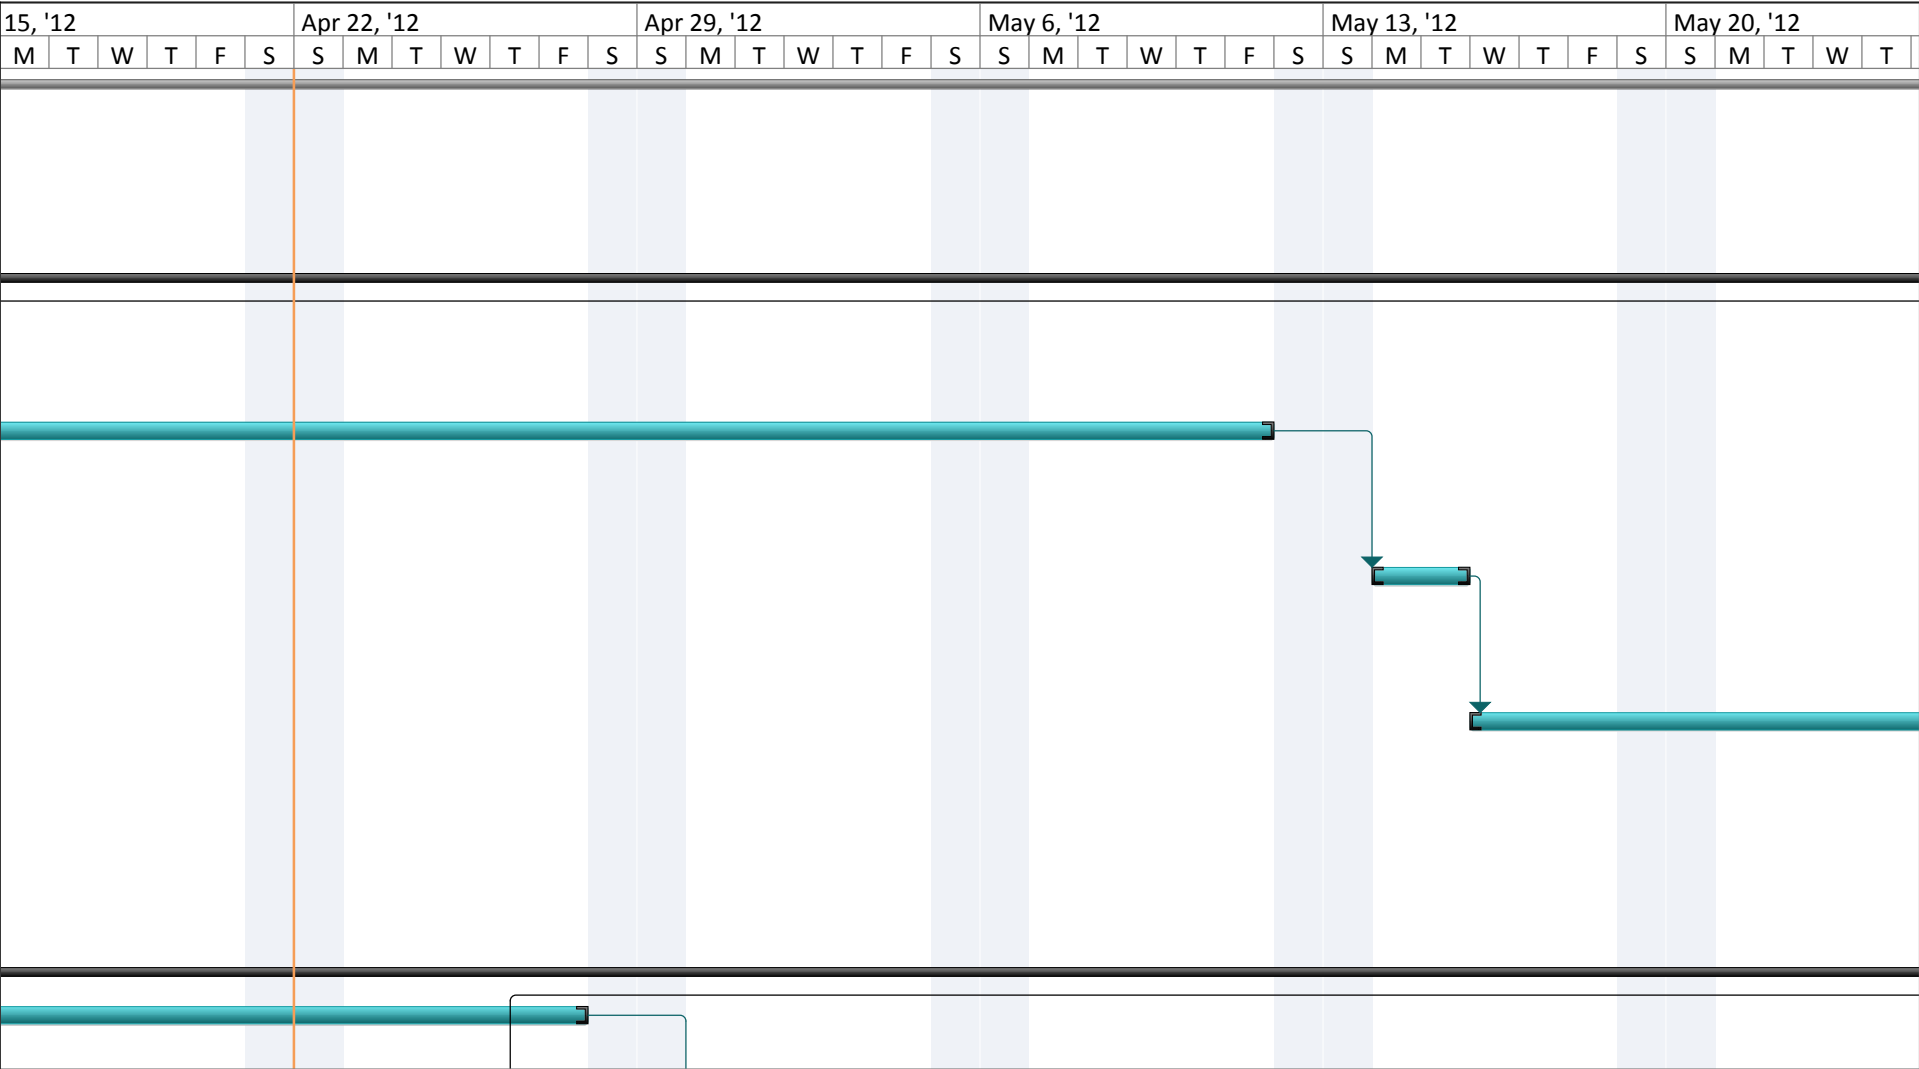


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

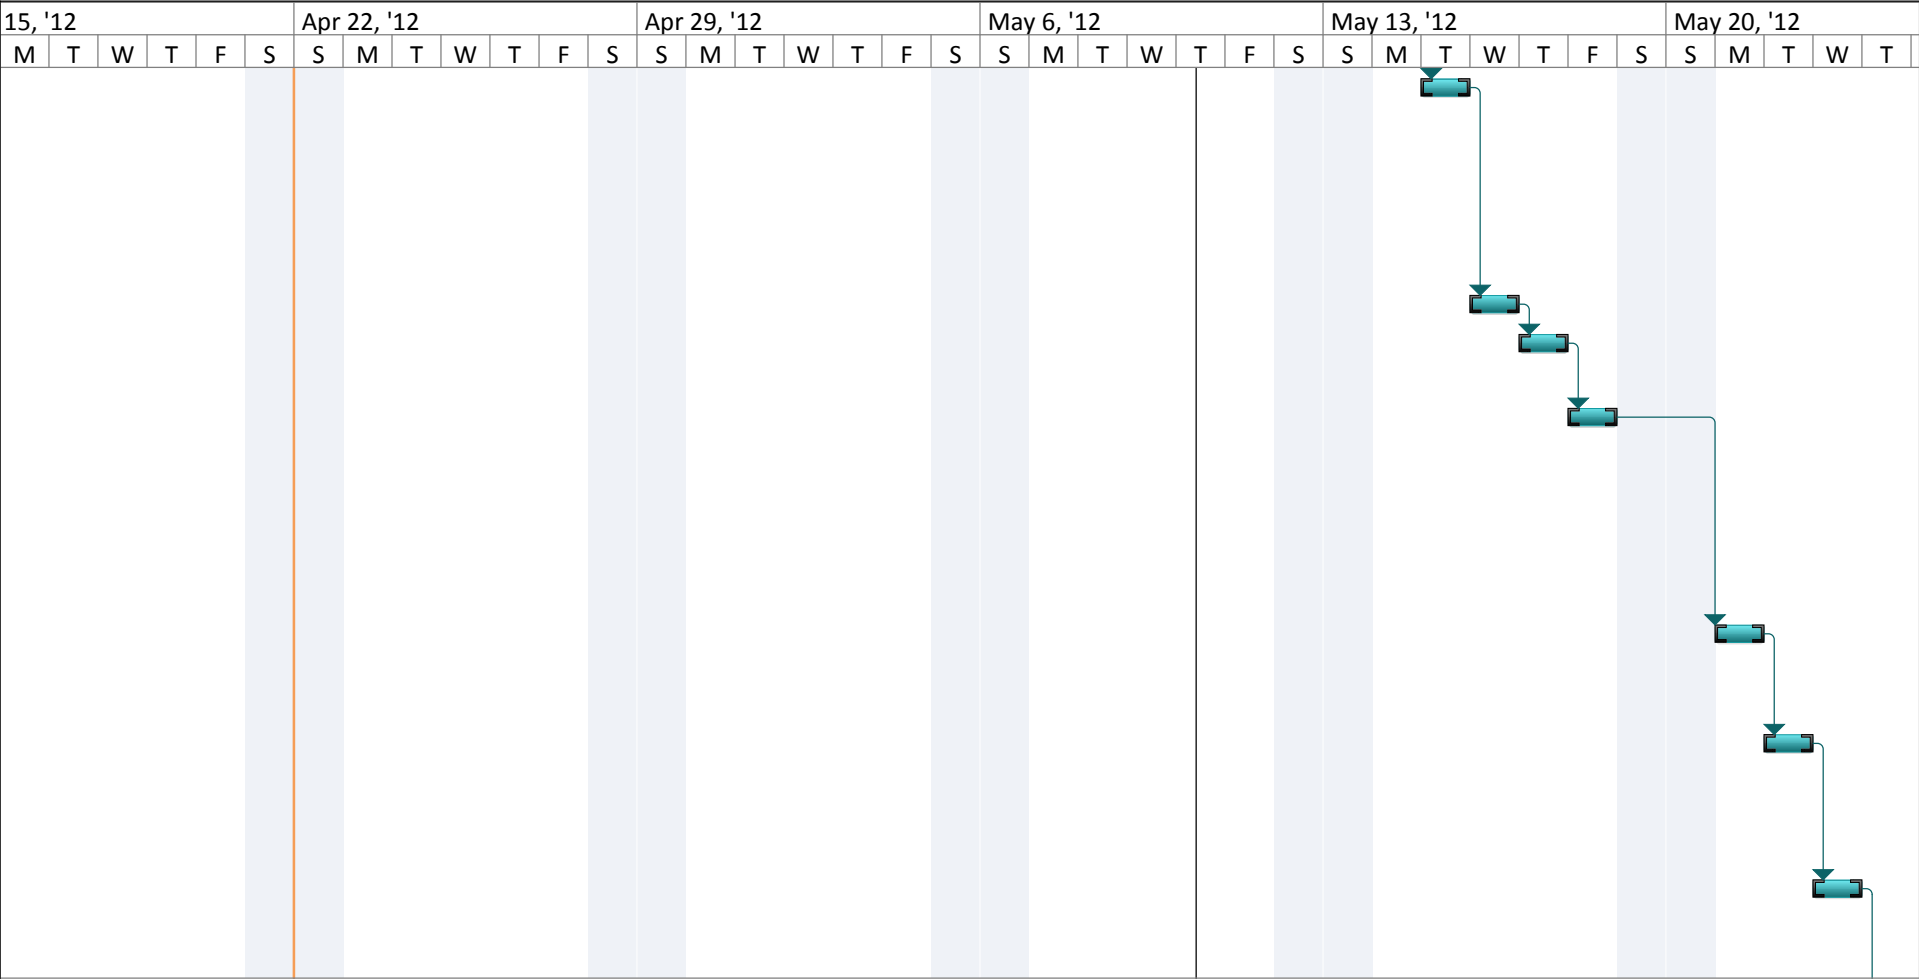

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

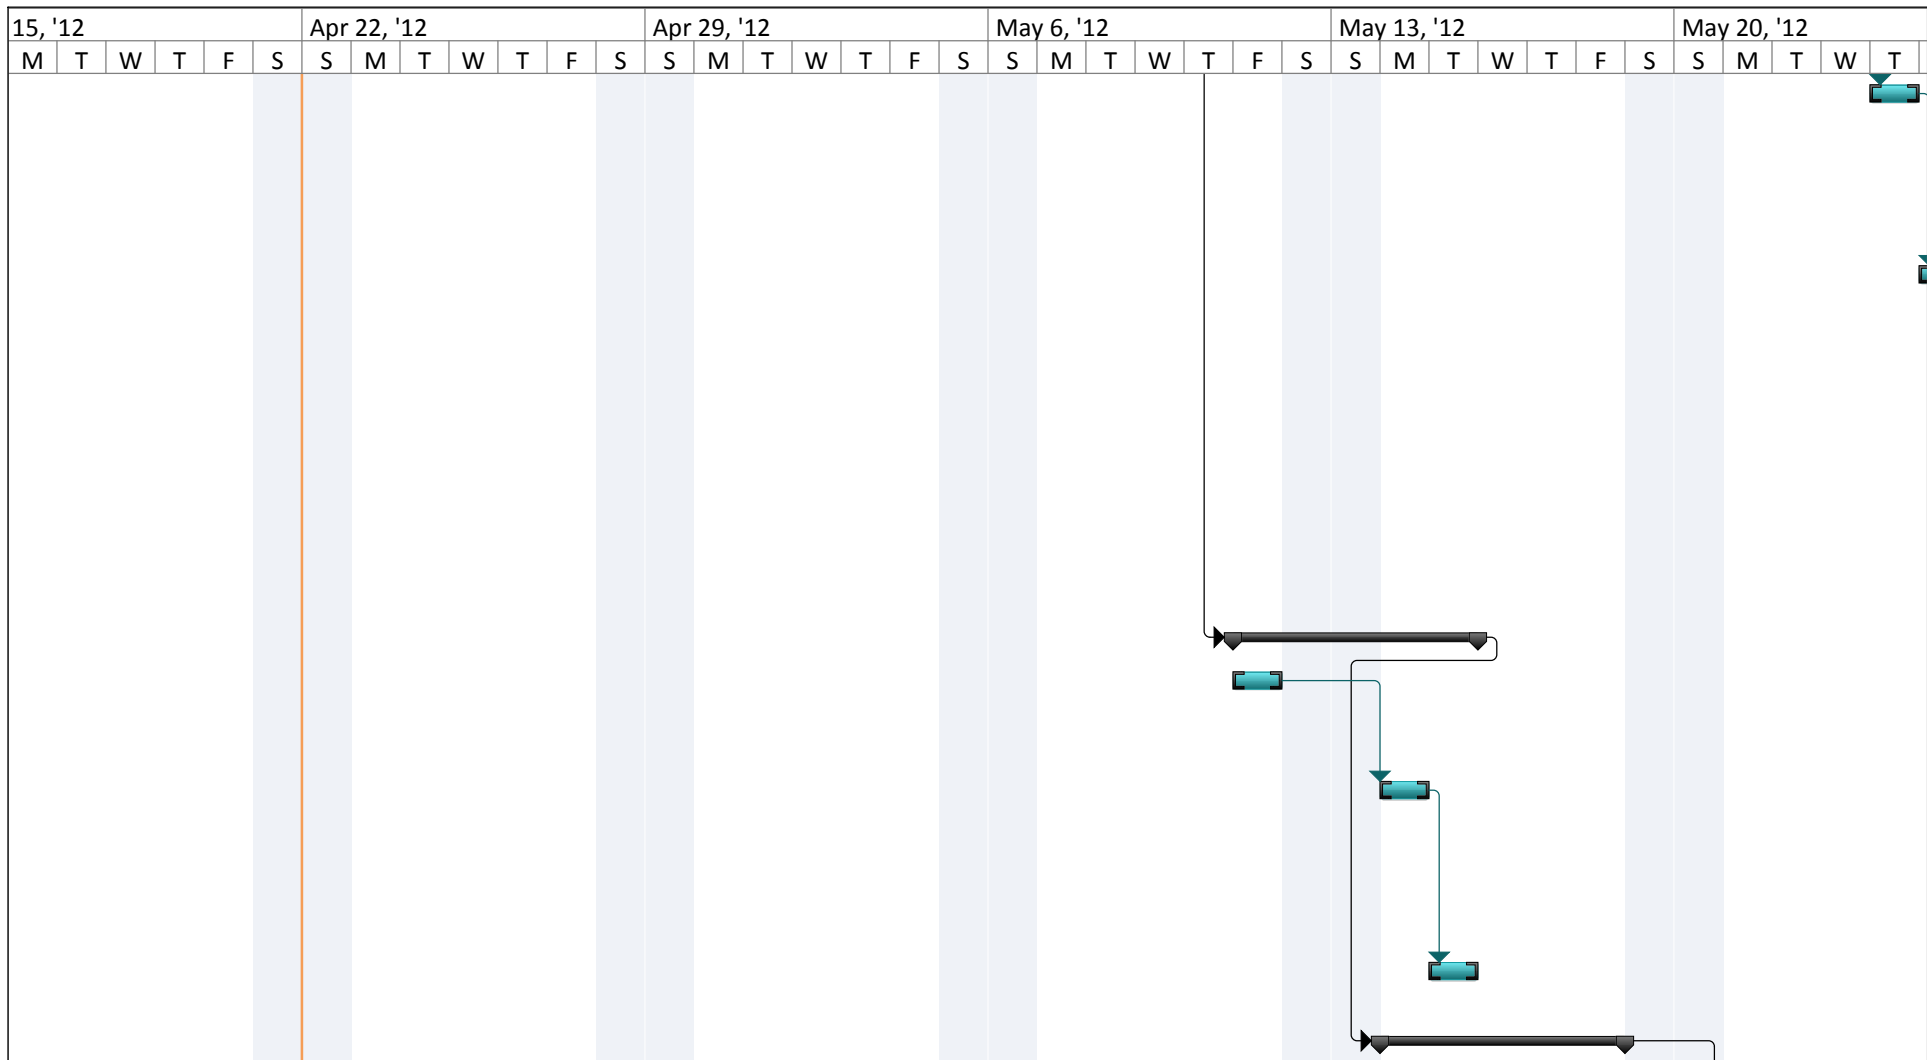


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

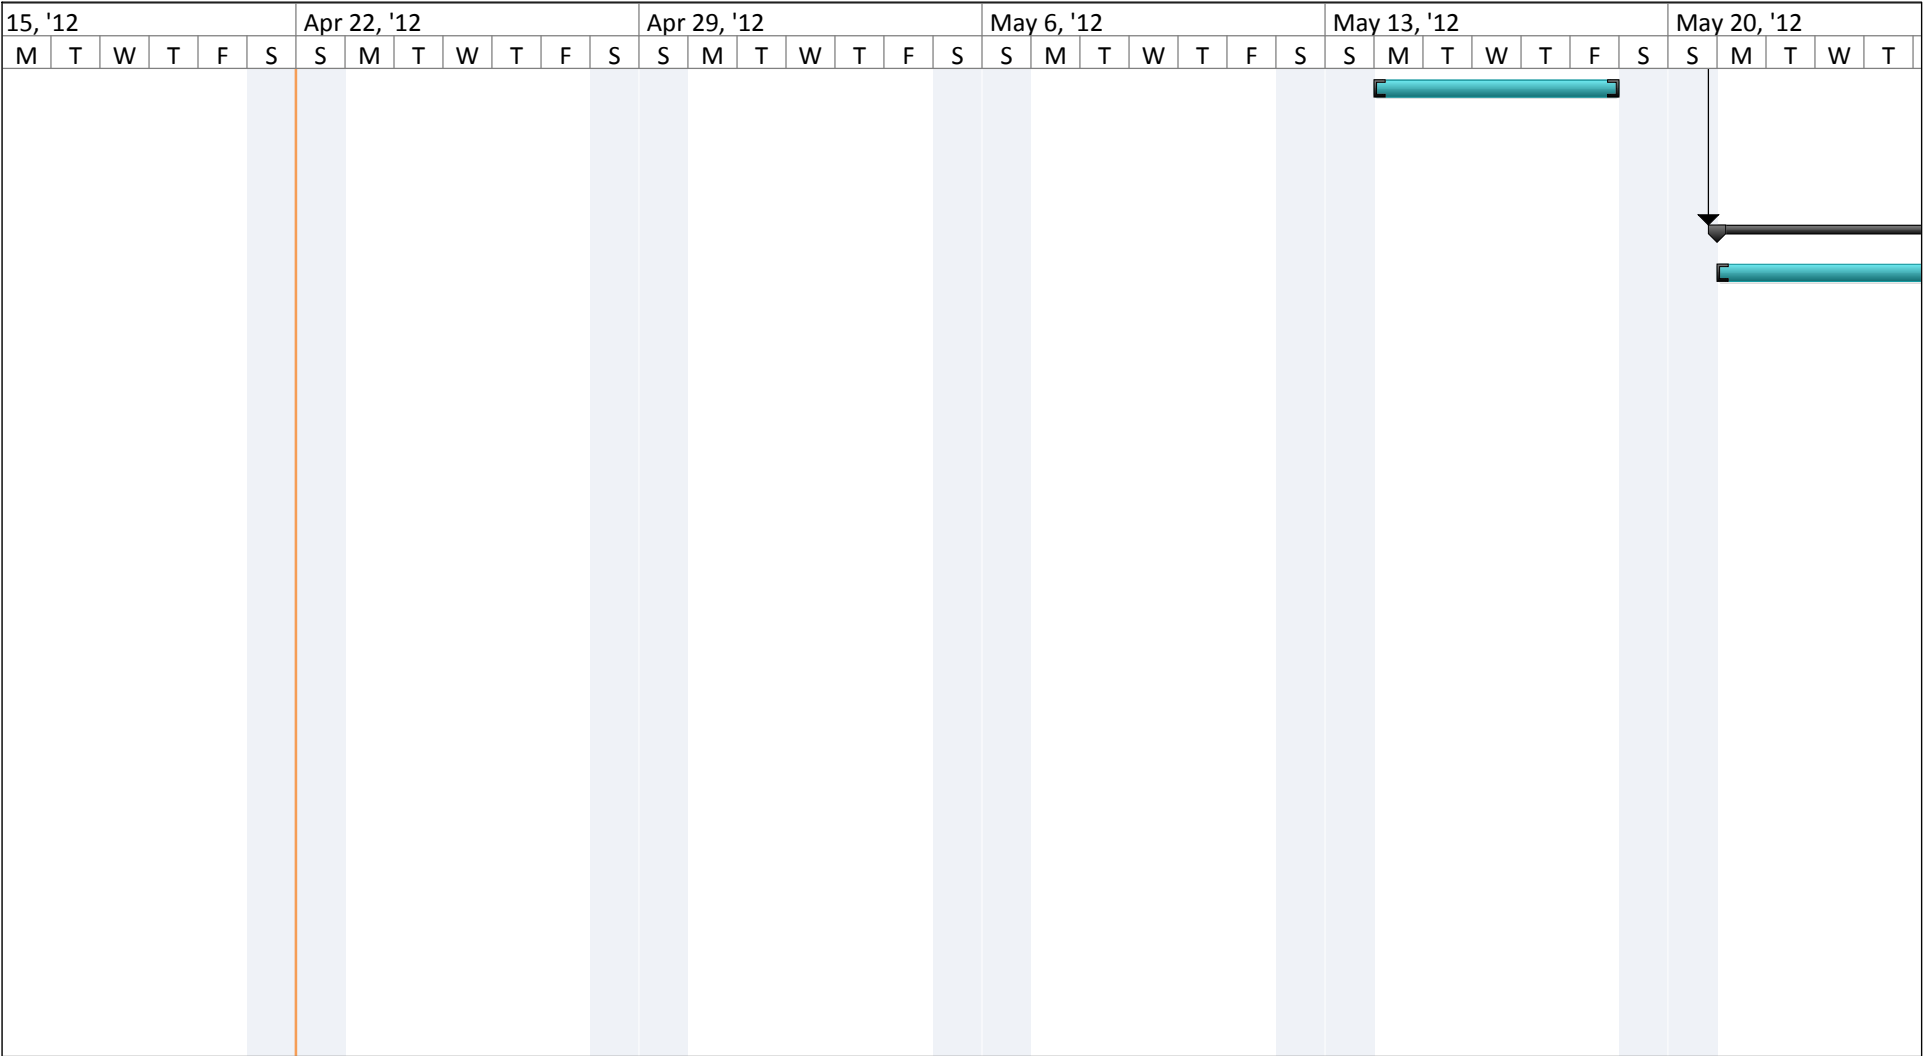


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

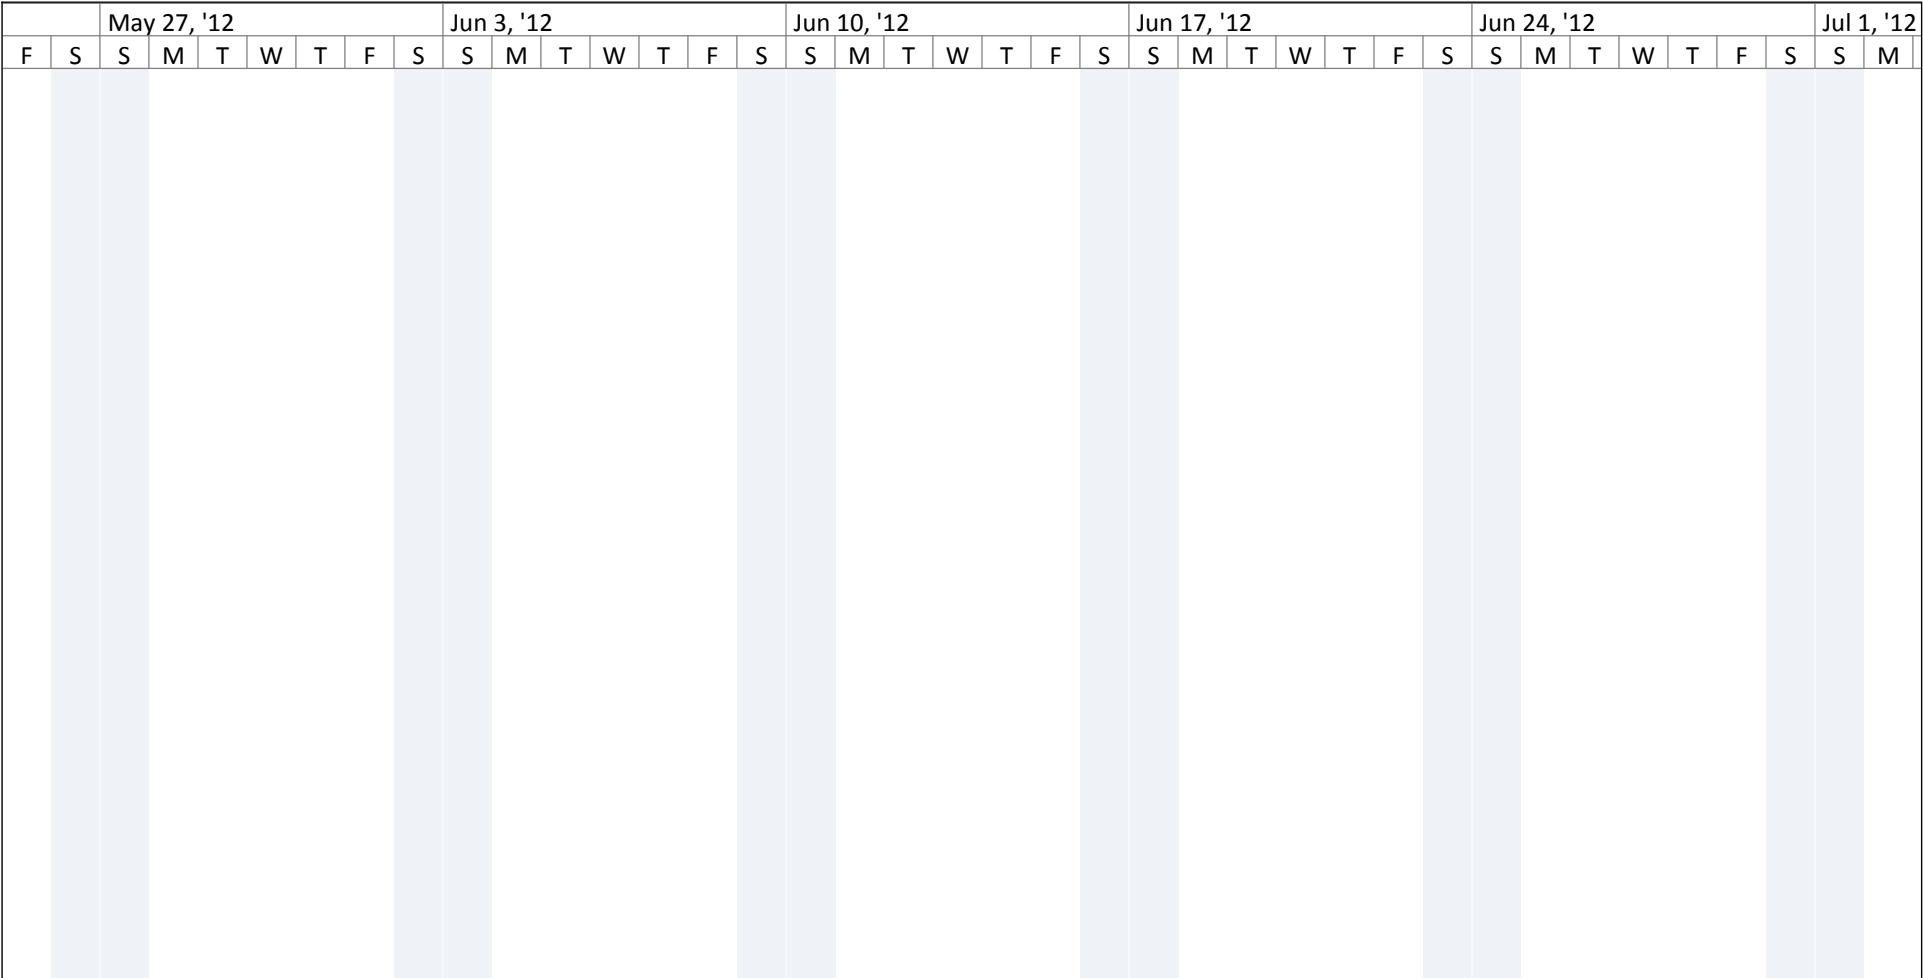


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

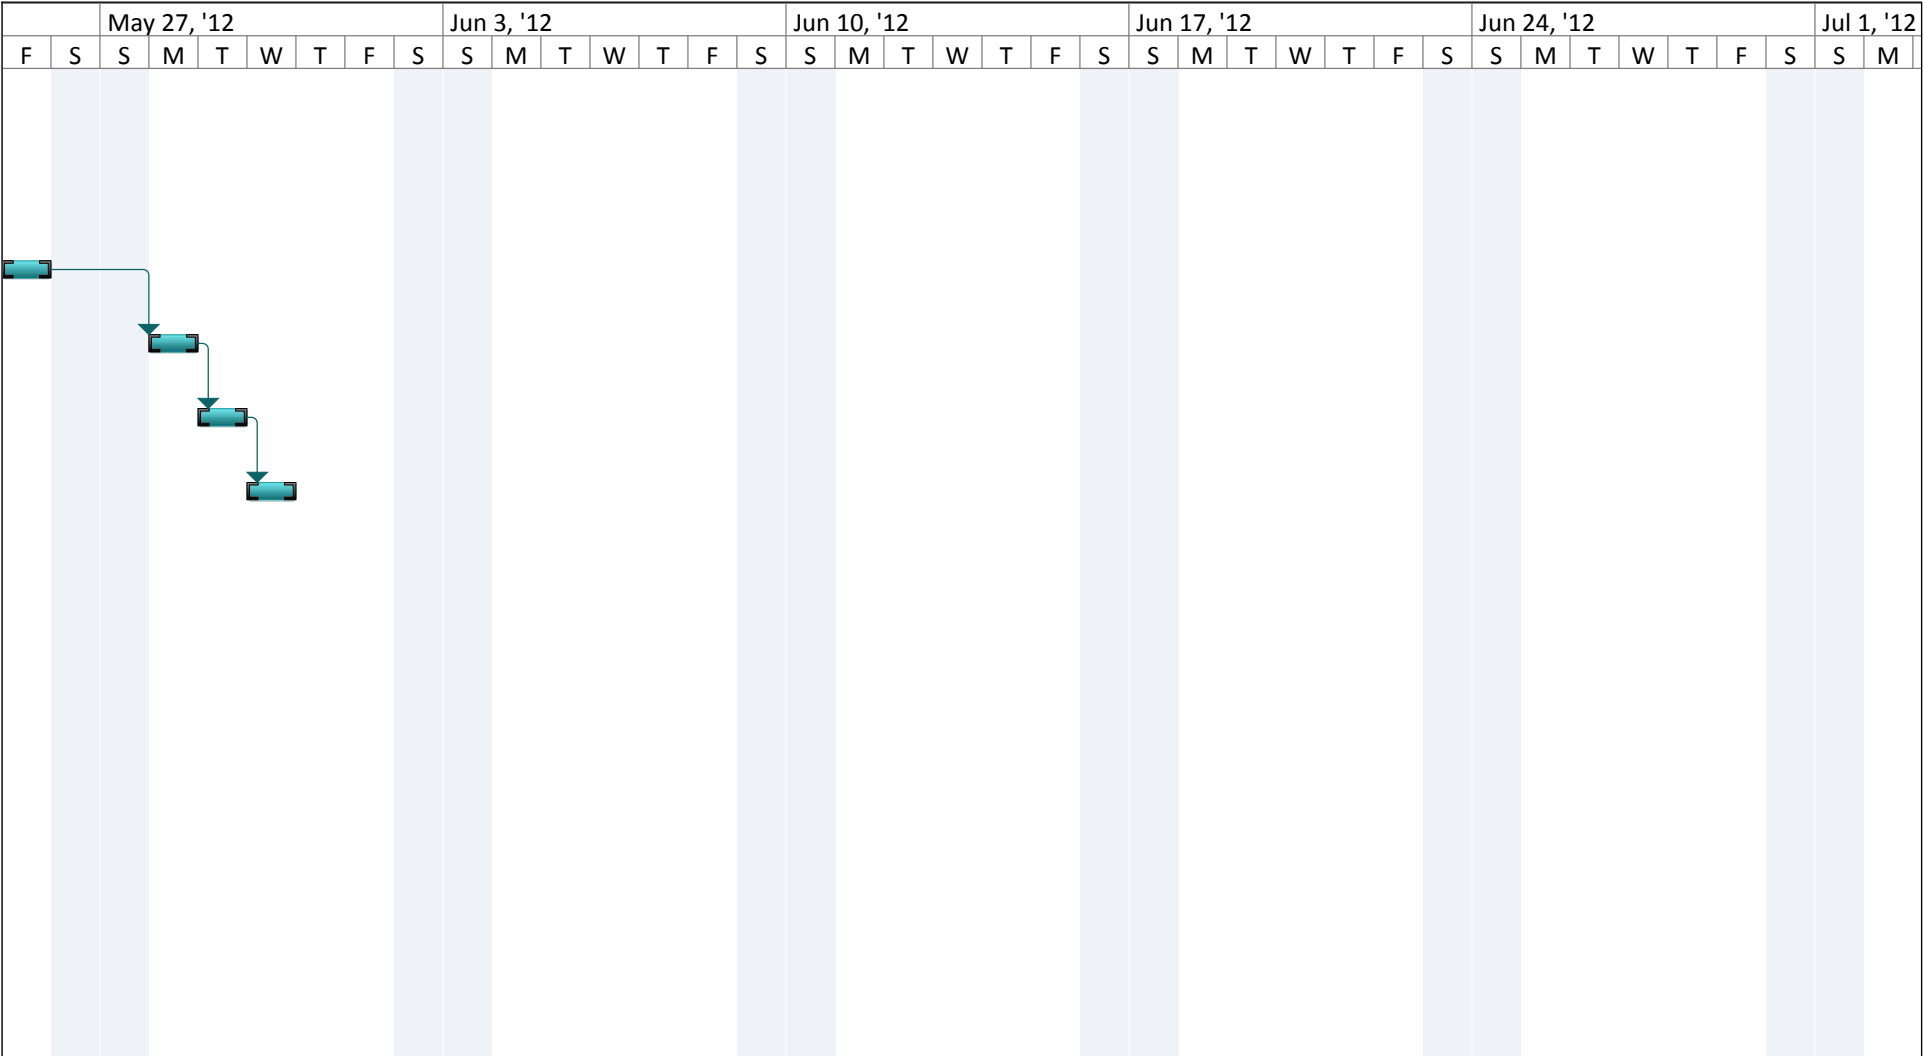


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

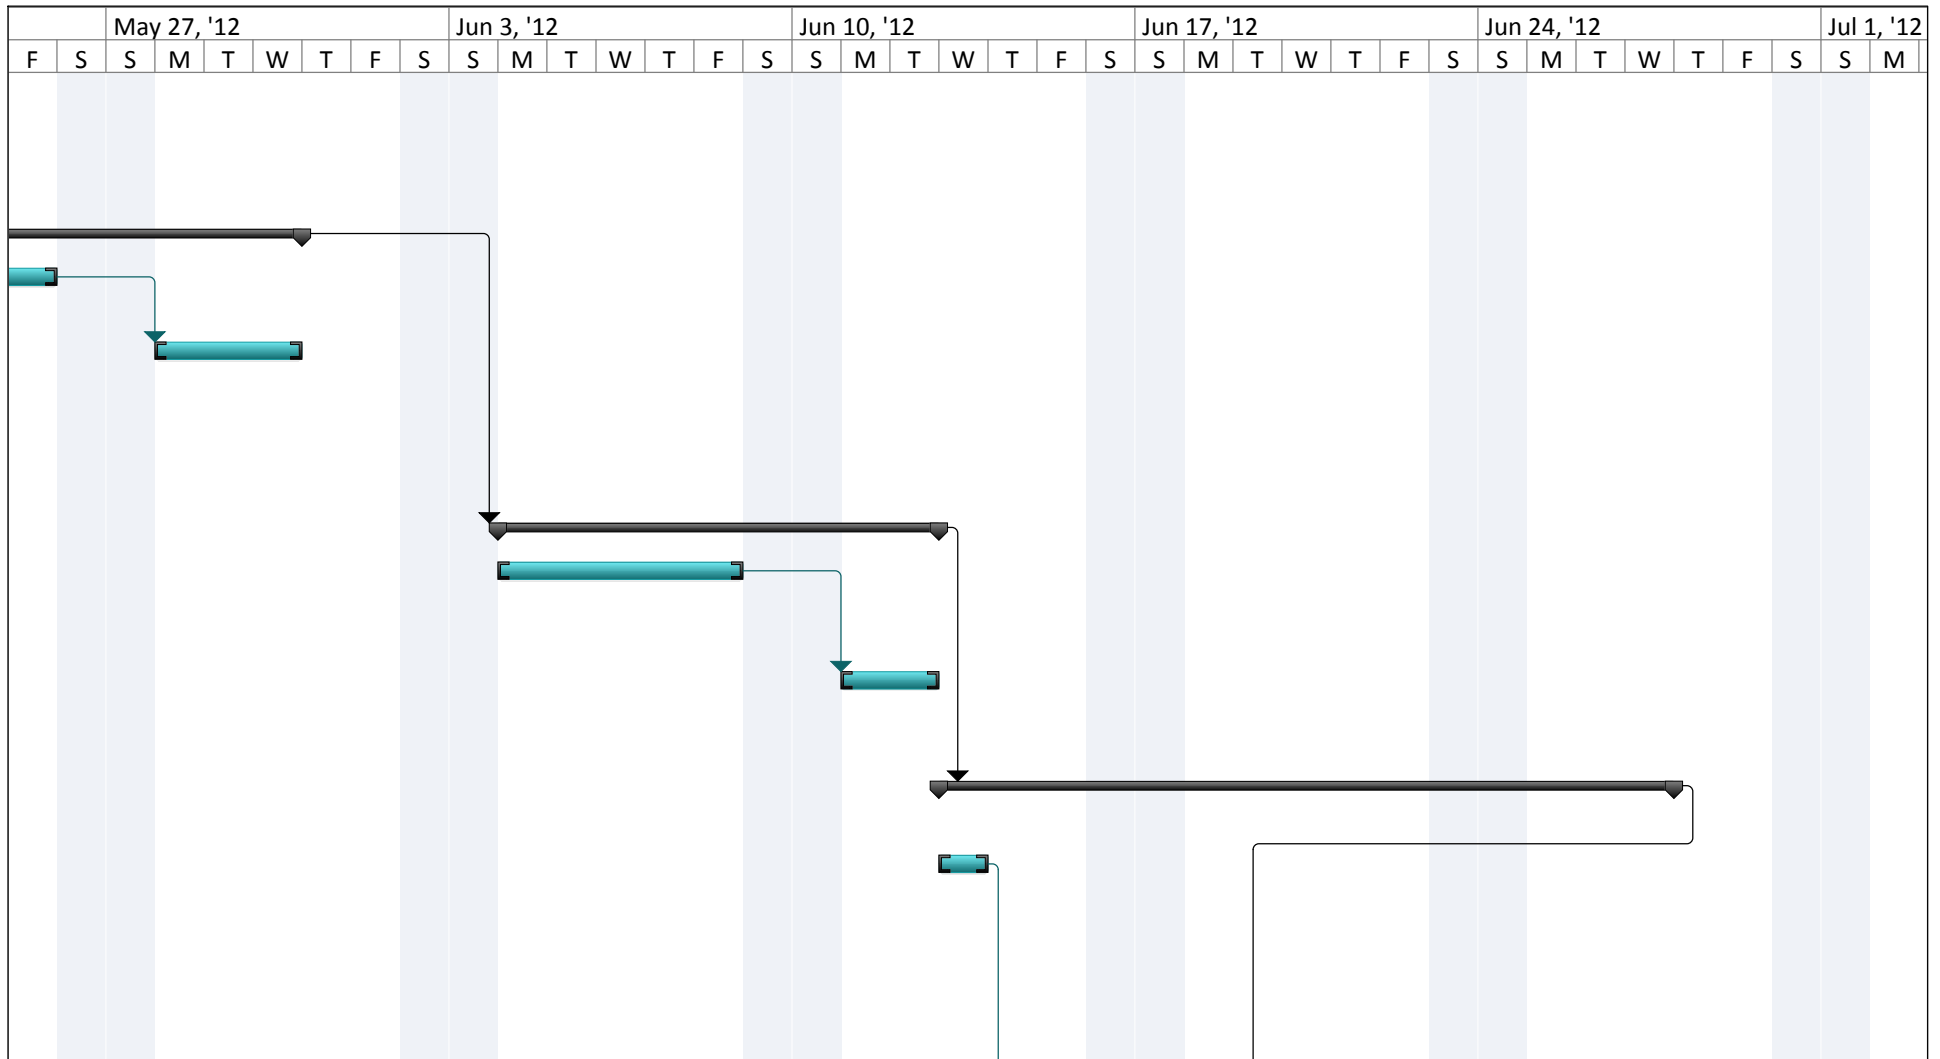


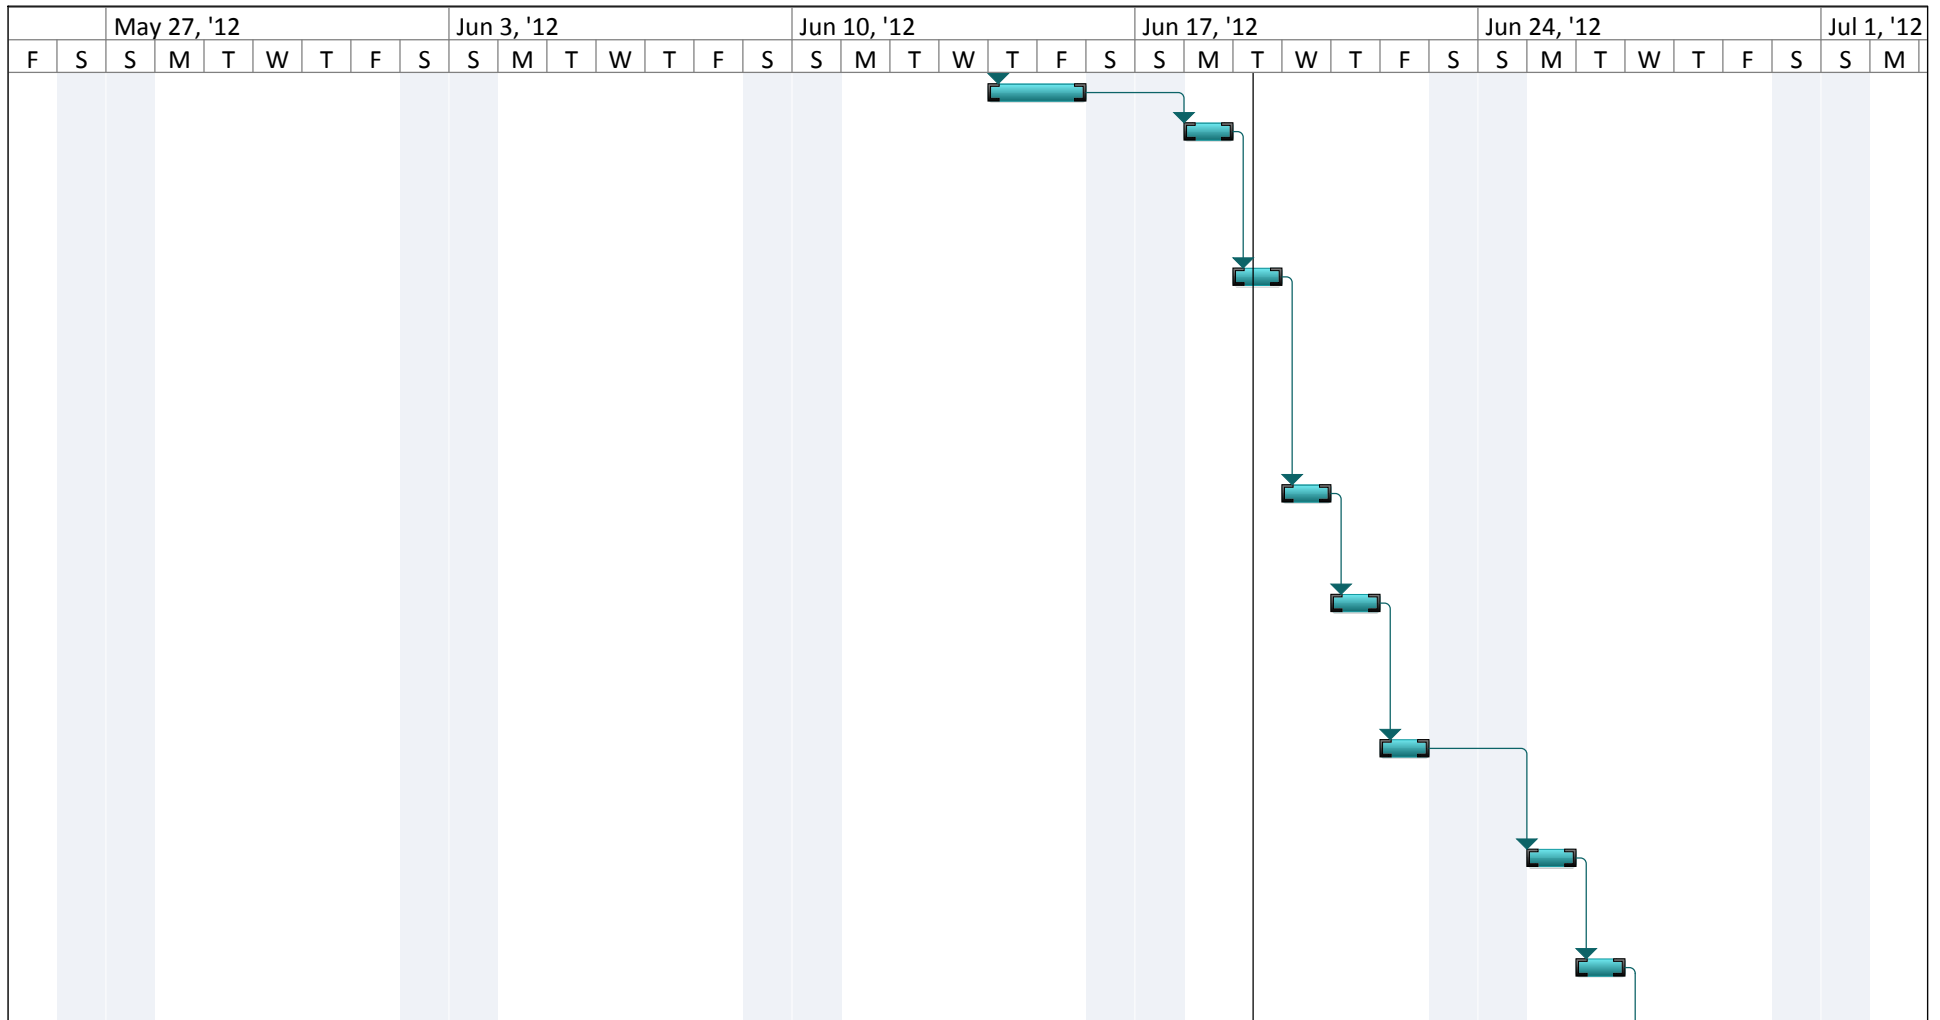


Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

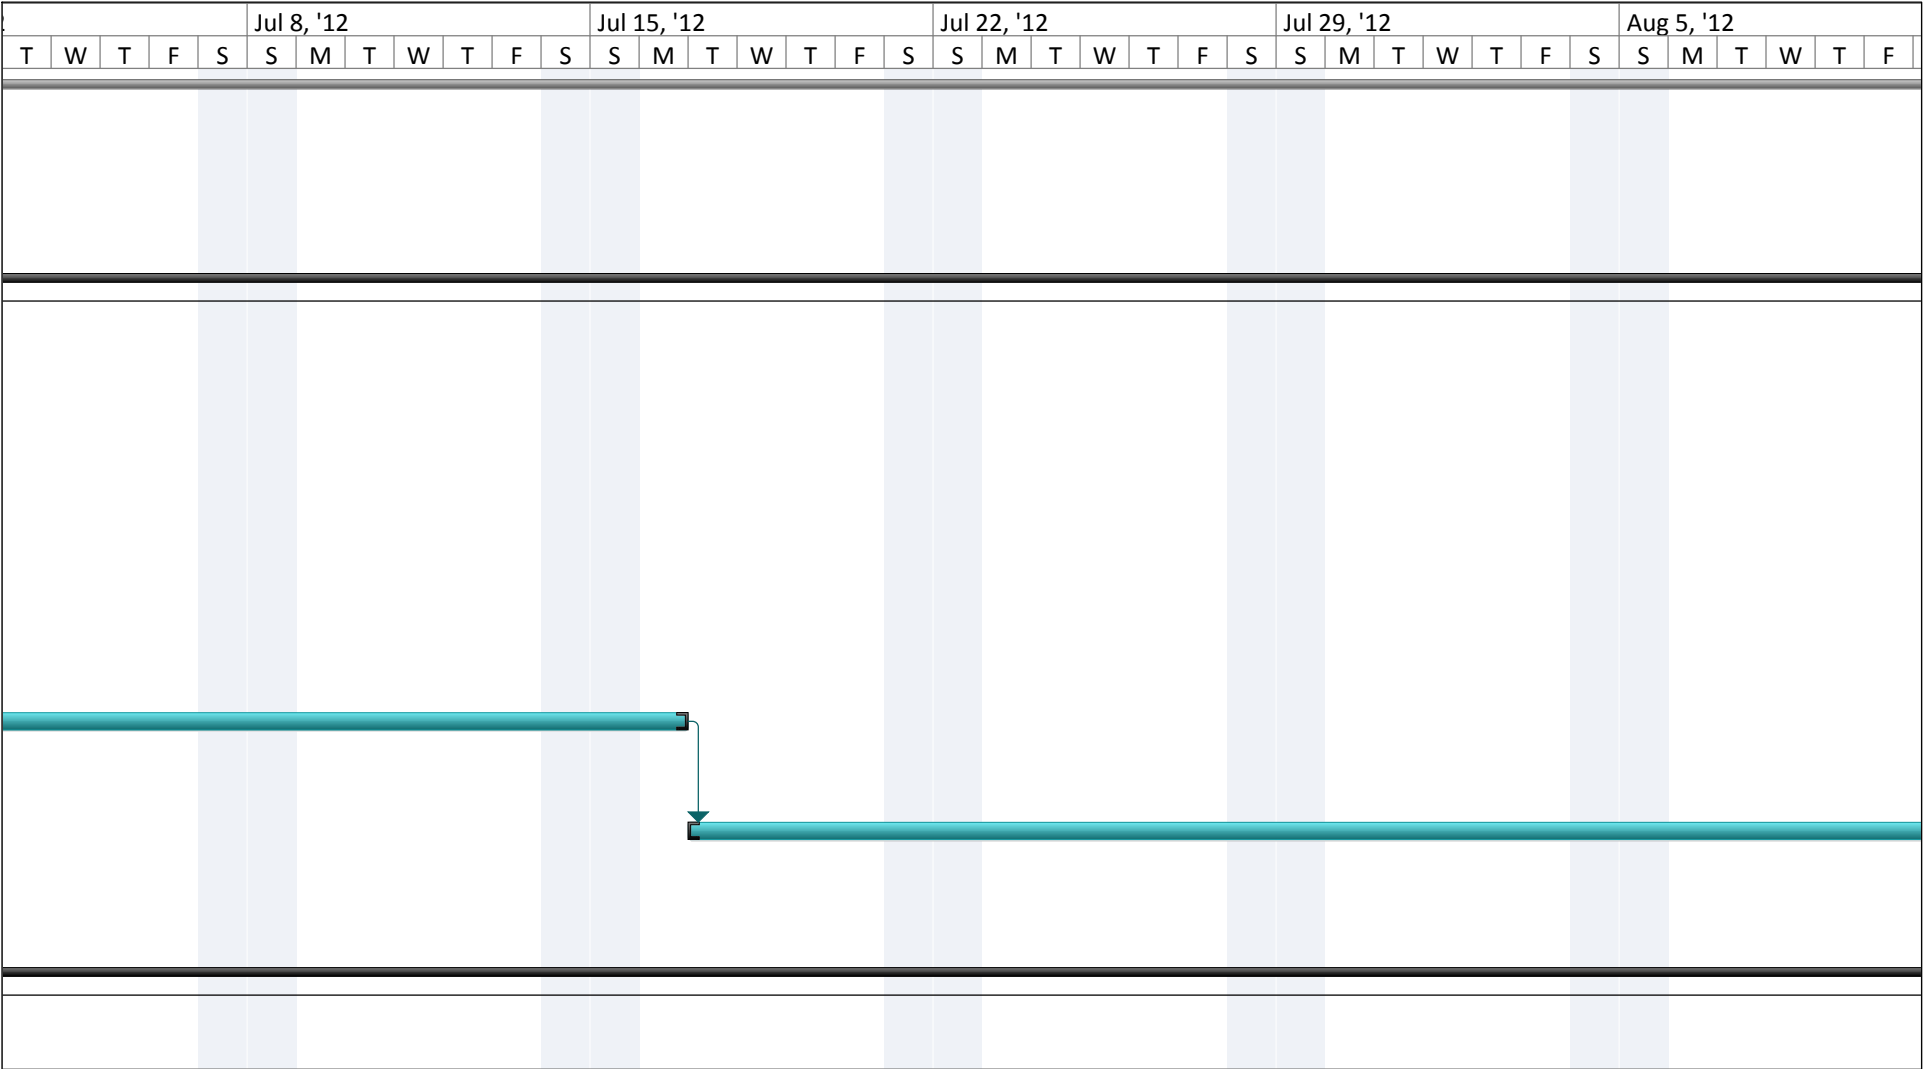

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

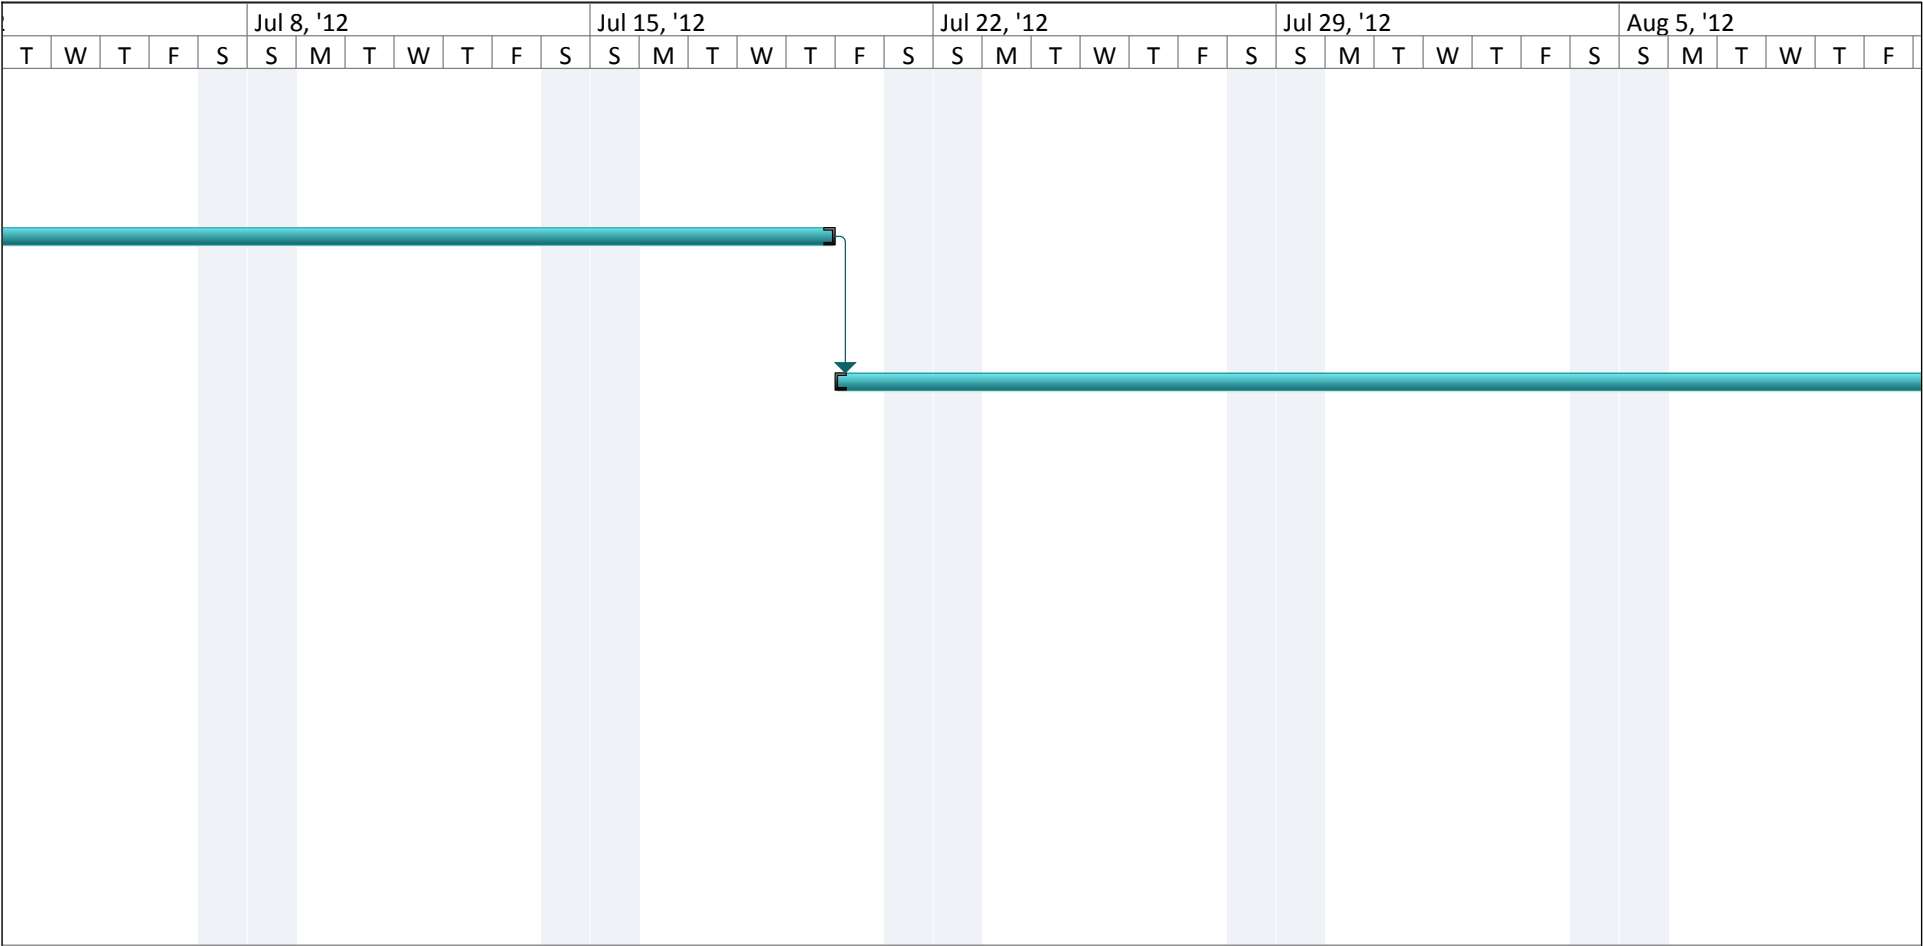

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

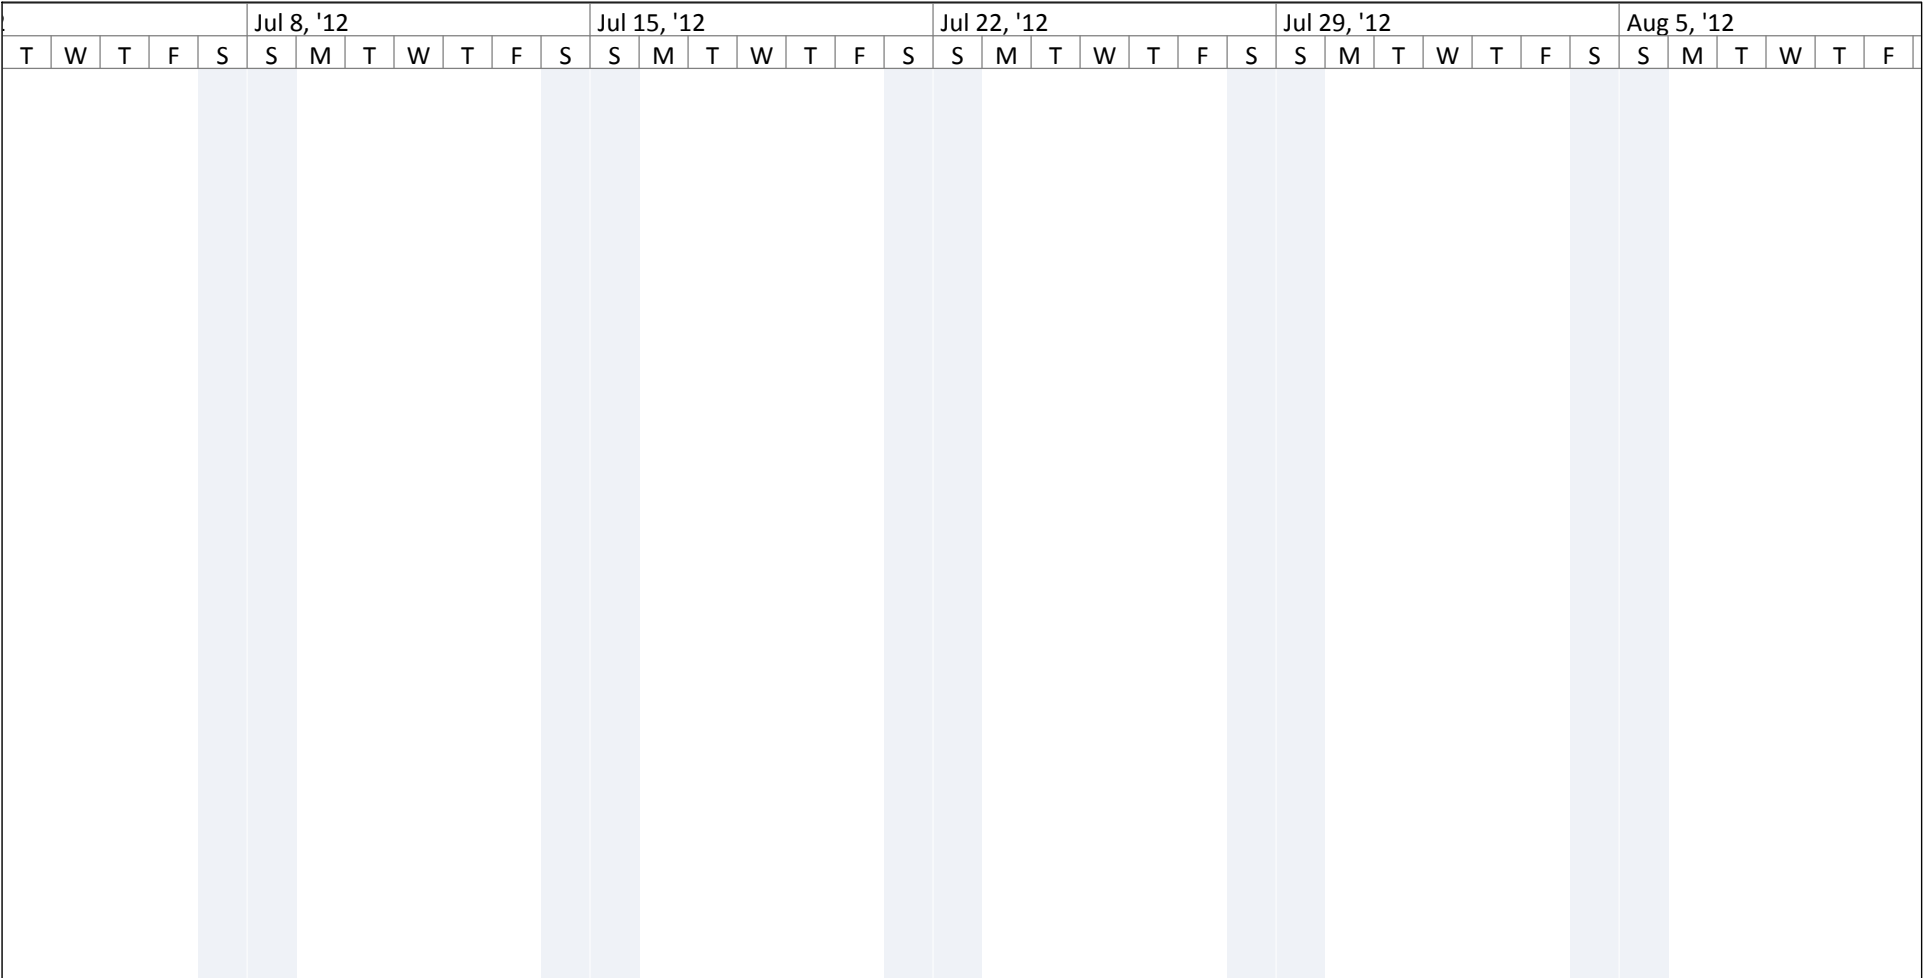

Project: EDR Website Redesign
Date: Sun 4/22/12

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only


Finish-only

Deadline

Progress

					Jul 8, '12							Jul 15, '12							Jul 22, '12							Jul 29, '12							Aug 5, '12						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

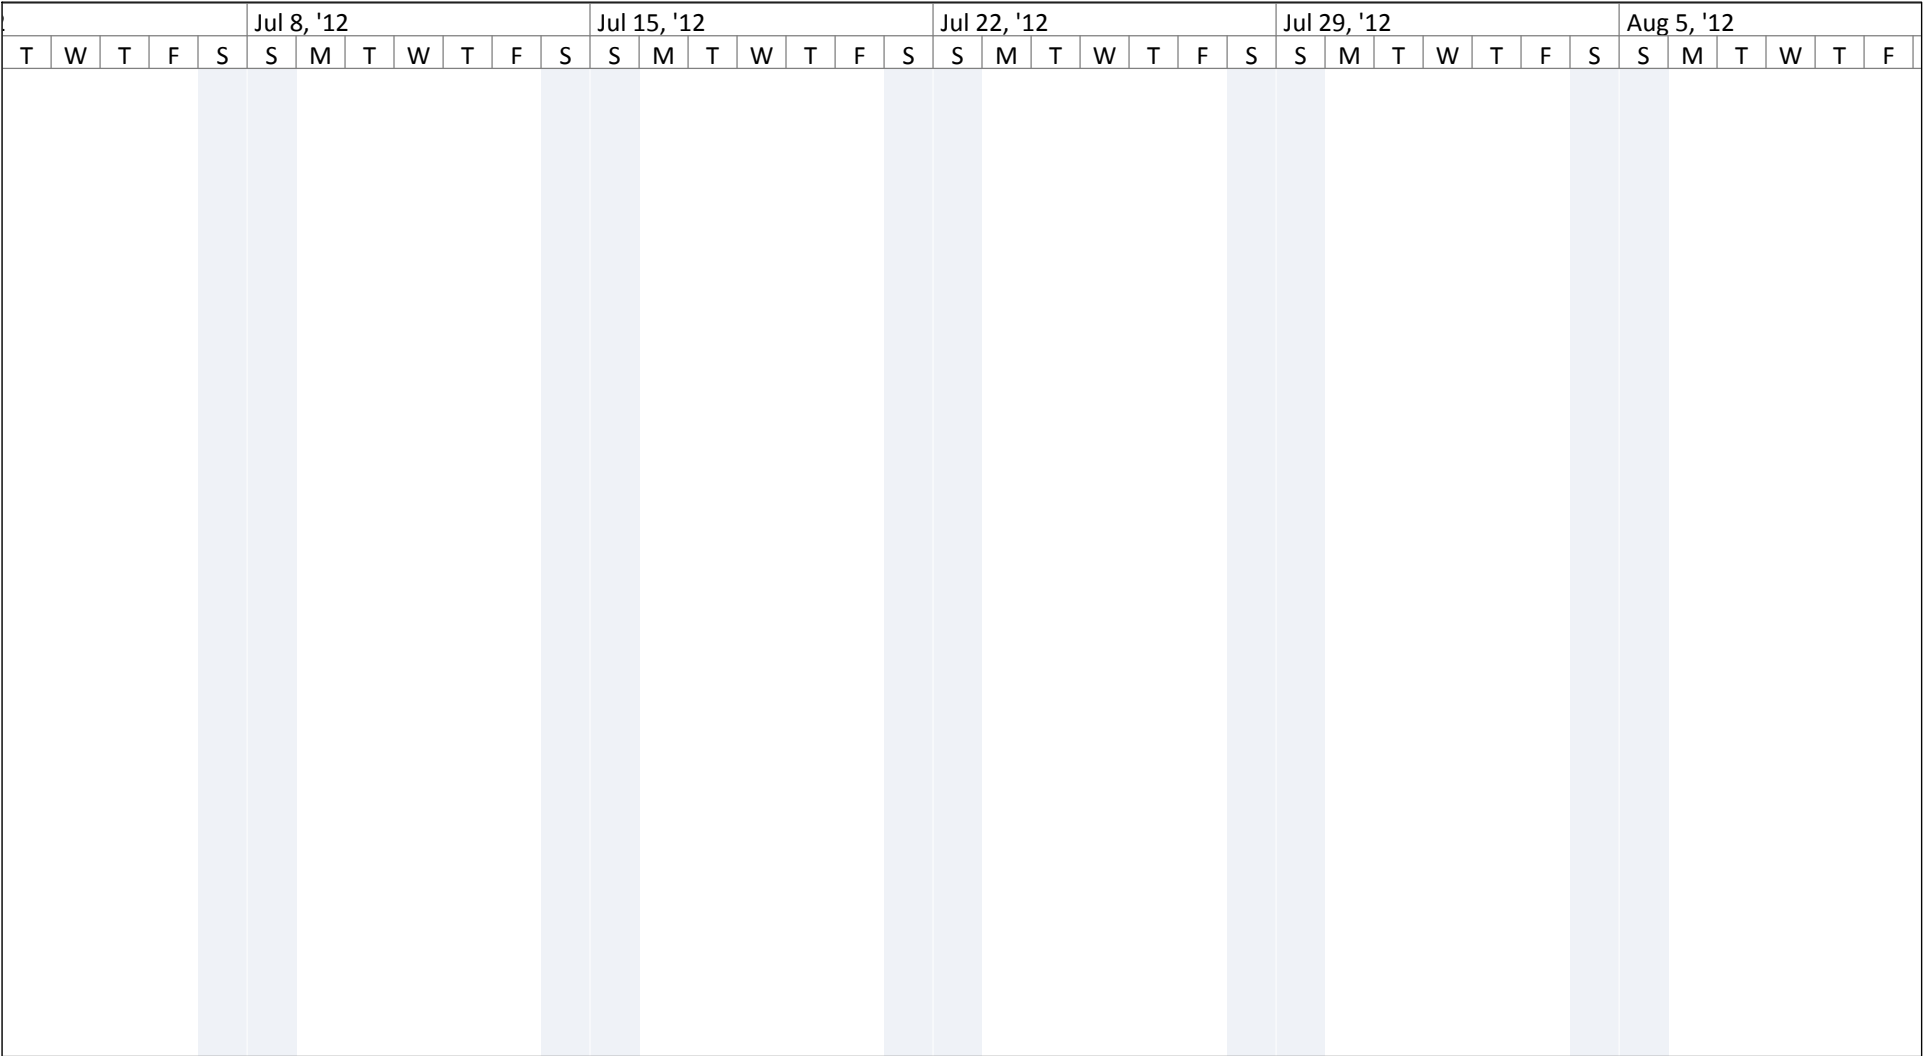

Project: EDR Website Redesign
Date: Sun 4/22/12

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

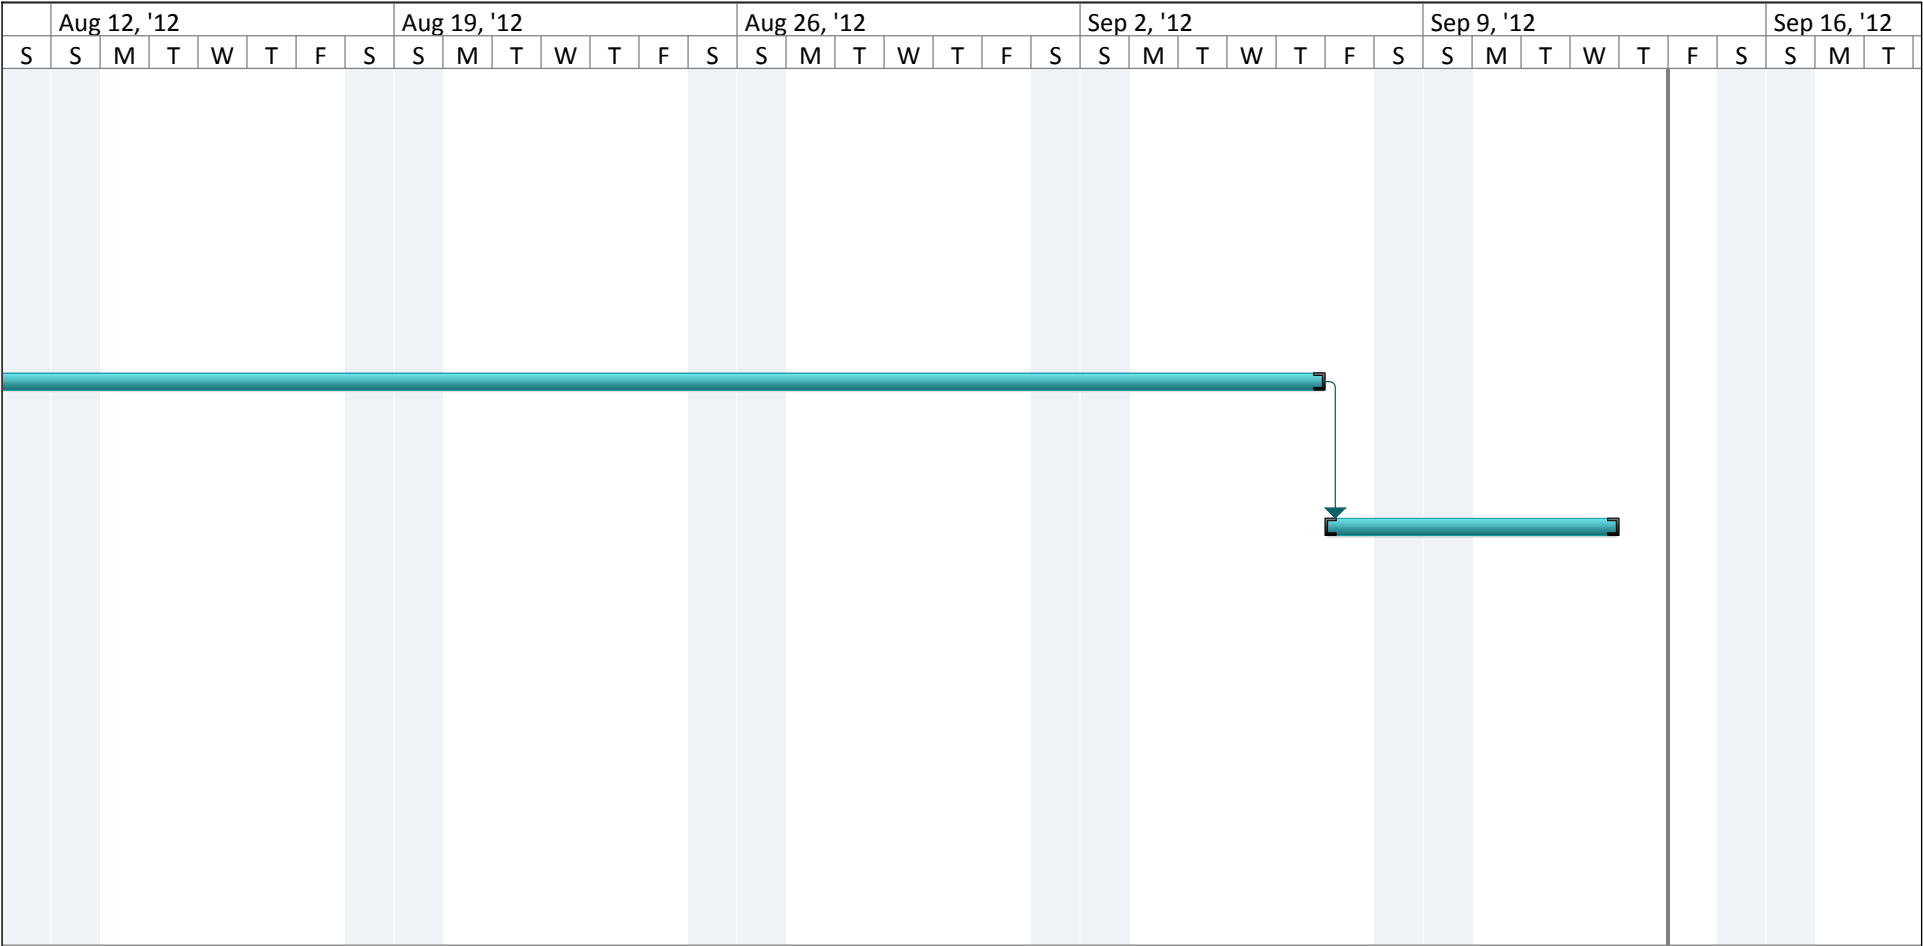

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Aug 12, '12							Aug 19, '12							Aug 26, '12							Sep 2, '12							Sep 9, '12							Sep 16, '12				
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	

--

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Aug 12, '12							Aug 19, '12							Aug 26, '12							Sep 2, '12							Sep 9, '12							Sep 16, '12			
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	F	S	S	M	T		

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Aug 12, '12							Aug 19, '12							Aug 26, '12							Sep 2, '12							Sep 9, '12							Sep 16, '12			
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	F	S	S	M	T		

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Aug 12, '12							Aug 19, '12							Aug 26, '12							Sep 2, '12							Sep 9, '12							Sep 16, '12				
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	

Project: EDR Website Redesign Date: Sun 4/22/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

